/Non Project/PSP for Engineers/Program 5

PSP2 Project Plan Summary

Project Settings

Project Owner	MITOME Shintaro
Start Date	2025 7月 05 03:44:48 午後
Completion Date	2025 7月 19 03:26:14 午後
Keywords	
Language	Java

Completed: ☑

Overall Metrics

Summary	**計画**	**実績値**	**累計値**
Size/Hour	10.4	13.2	13.2
Planned Time	4:21		4:21
実績値 時間		5:45	5:45
CPI (Cost-Performance Index)			0.76
% Reuse	0%	0%	0%
% New Reusable	0%	11.8%	11.8%
Test Defects/KLOC or equivalent	43.2	0	0
Total Defects/KLOC or equivalent	140	92.1	92.1
Yield %	66.2%	77.8%	77.8%
Code Review Rate	135	163	163

Program Size

	計画	**実績値**	**累計値**
Base (B)	138	138	138
Deleted (D)	53	63	63
Modified (M)	9	1	1
Added (A)	36.1	75	75
Reused (R)	0	0	0
Added and Modified (A+M)	45.1	76	76
Total Size (T)	121	150	150
Total New Reusable	0	9	9

Estimated Proxy Size (E)	44.7	76	76

Time In Phase

	計画	実績値	累計値	累計値 (%)
計画立案	1:12	1:40	1:40	29.0%
設計	0:24	0:37	0:37	10.7%
設計レビュー	0:20	0:28	0:28	8.12%
コーディング	1:09	1:47	1:47	31.0%
コードレビュー	0:20	0:28	0:28	8.12%
コンパイル	0:11	0:00	0:00	0%
テスト	0:20	0:03	0:03	0.87%
事後分析	0:25	0:42	0:42	12.2%
合計	4:21	5:45	5:45	

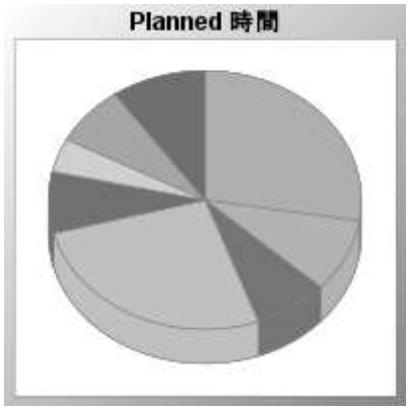

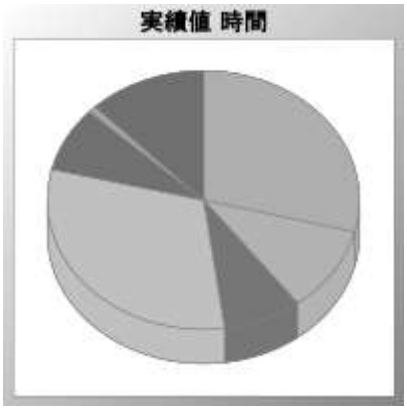

Defects Injected

	計画	実績値	累計値	累計値 (%)
開発前	0	0	0	0%
計画立案	0.58	1	1	11.1%
設計	0.92	2	2	22.2%
設計レビュー	0	0	0	0%
コーディング	4.72	6	6	66.7%
コードレビュー	0	0	0	0%
コンパイル	0.12	0	0	0%
テスト	0	0	0	0%
合計	6.33	9	9	

Defects Removed

	計画	実績値	累計値	累計値 (%)
計画立案	0	0	0	0%
設計	0	0	0	0%
設計レビュー	0.9	2	2	28.6%
コーディング	0.19	1	1	14.3%
コードレビュー	3.02	4	4	57.1%
コンパイル	0.27	0	0	0%
テスト	1.95	0	0	0%
合計	6.33	7	7	
After Development	0	2	2	

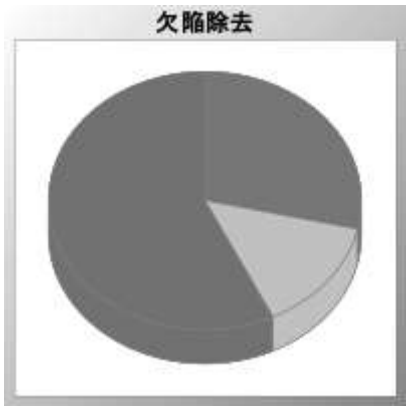

Defect Removal Efficiency

	計画	実績値	累計値
Defects/Hour - Design Review	2.7	4.29	4.29
Defects/Hour - Code Review	9.06	8.57	8.57
Defects/Hour - Compile	1.47	#DIV/0!	#DIV/0!
Defects/Hour - Test	5.98	0	0
DRL (DLDR/UT)	0.45	#DIV/0!	#DIV/0!
DRL (Code Review/UT)	1.52	#DIV/0!	#DIV/0!

DRL (Compile/UT)	0.25	#DIV/0!	#DIV/0!

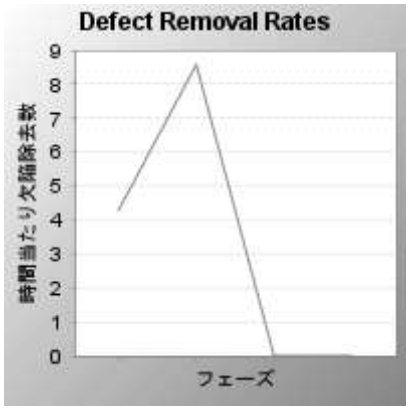

PSP materials copyright © 2018 Carnegie Mellon University, licensed under CC BY 4.0.
