# 獲得価値 - prog5

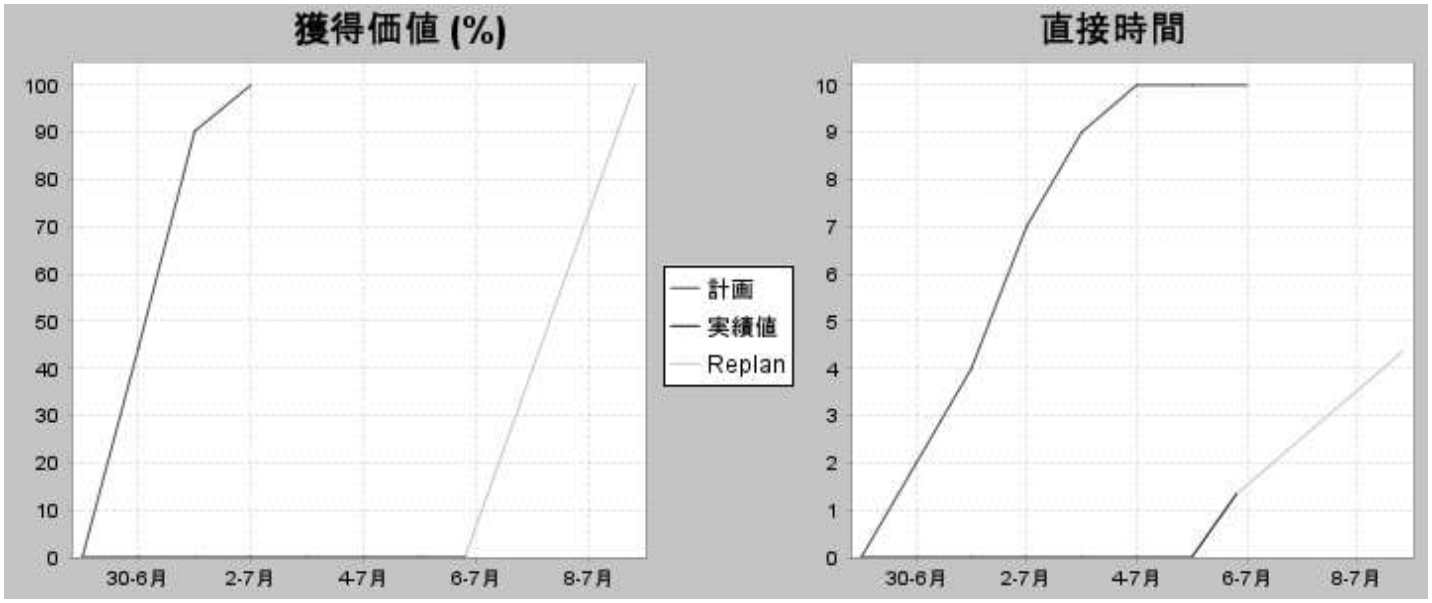
獲得価値 (%)
100
90
80
70
60
50
40
30
20
10
0
30-6月
2-7月
4-7月
6-7月
8-7月
計画
実績値
Replan
直接時間
10
9
8
7
6
5
4
3
2
1
0
30-6月
2-7月
4-7月
6-7月
8-7月

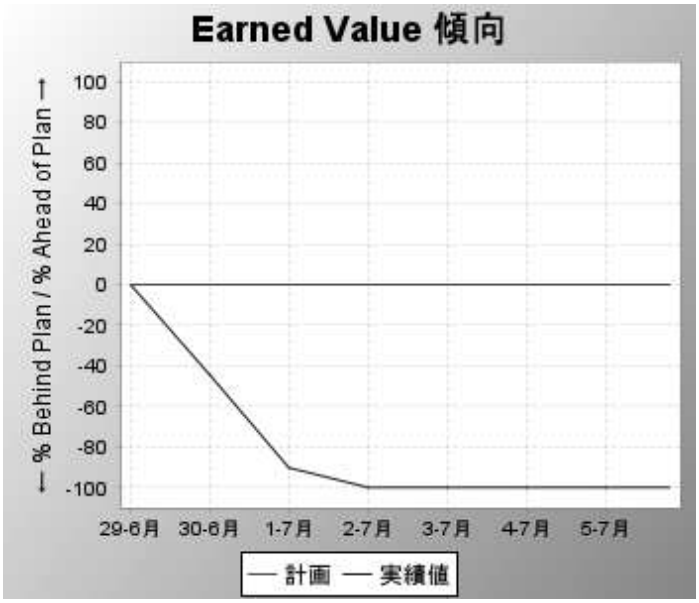
Earned Value 傾向
← % Behind Plan / % Ahead of Plan →
100
80
60
40
20
0
-20
-40
-60
-80
-100
29-6月
30-6月
1-7月
2-7月
3-7月
4-7月
5-7月
計画
実績値

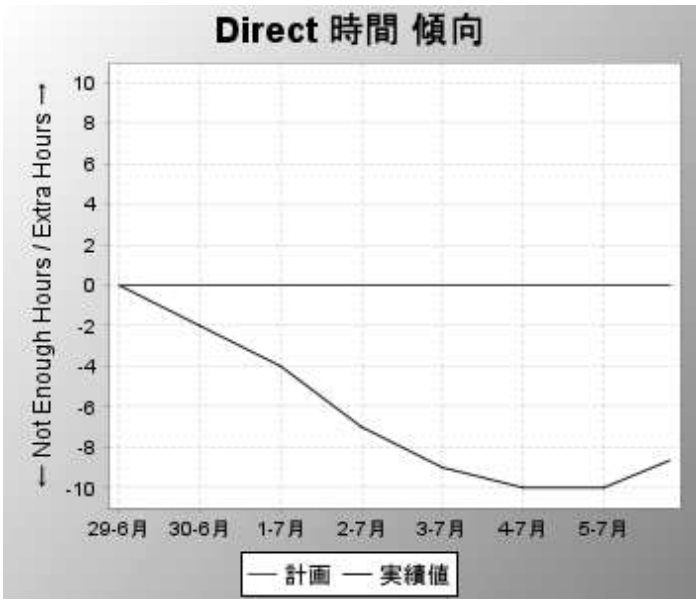
Direct 時間 傾向
← Not Enough Hours / Extra Hours →
10
8
6
4
2
0
-2
-4
-6
-8
-10
29-6月
30-6月
1-7月
2-7月
3-7月
4-7月
5-7月
計画
実績値

| | | |
|---|---|---|
| **Planned Completion Date:** | 2025/07/01 | *(Based upon the planned time for each task and the planned time in your schedule, you plan to complete the work by 2025/07/01.)* |
| **Replanned Completion Date:** | 2025/07/08 | *(If you were to "replan from today," taking into account the amount of time your actual progress has slipped against your original plan, but assuming that your original planned times still hold true for all remaining tasks and time periods, the replanned completion date for the overall work would be 2025/07/08.)* |
| **Replanned Cost:** | 4.35 | *(Based on your current cost variance, the total work is projected to require 4.35時間 of effort if remaining tasks take exactly as much time as planned.)* |
| **コスト差異(CV):** | 0 | *(現在までに 完了したタスクは計画に比べ 0分 少ない 作業工数が掛かりました。)* |
| **スケジュール差異(SV):** | -4.35 | *(今日までに完了していると計画した作業に比べ、4.35時間 少ない 作業が完了しています。)* |
| **スケジュール差異 (%SV):** | -100% | *(今日までに完了していると計画した作業に比べ、100% 少ない 作業が完了しています。)* |
| **スケジュール効率指数(SPI):** | 0 | *(スケジュールより送れてタスクが完了しています。今までに達成しているべき作業１時間あたり、0時間の作業が完了しています。これは当初のスケジュール計画が、挑戦的すぎたことを意味するかもしれません。)* |
| **完了率(%):** | 0% | *(全作業中の0%を完了しています。)* |
| **経過率(%):** | 0% | *(全ての計画作業時間中 0% の作業時間が経過しました。)* |
| **残作業の効率指標:** | 1 | *(当初の見積もり工数の範囲内で全ての作業を完了するためには、これから１時間あたりに計画時における1時間の価値を達成しなければなりません。)* |

# タスクリスト

| プロジェクト/タスク | 計画時間 | 実績時間 | 計画価値 | 計画完了日 | Replan | 予測 | 実績完了日 | 依存 | 完了率(%) | 経過率(%) | 獲得価値 |
|---|---|---|---|---|---|---|---|---|---|---|---|
| prog5/Non Project/PSP for Engineers/Program 5 | 4:21 | 1:20 | 100% | 2025/07/01 | 2025/07/08 | | | | | 31% | |
| Planning | 1:12 | 1:20 | 27.6% | 2025/06/29 | 2025/07/05 | | | | | 111% | |
| Design | 0:24 | 0:00 | 9.2% | 2025/06/29 | 2025/07/06 | | | | | | |
| Design Review | 0:20 | 0:00 | 7.7% | 2025/06/29 | 2025/07/06 | | | | | | |
| Code | 1:09 | 0:00 | 26.4% | 2025/06/30 | 2025/07/07 | | | | | | |
| Code Review | 0:20 | 0:00 | 7.7% | 2025/06/30 | 2025/07/07 | | | | | | |
| Compile | 0:11 | 0:00 | 4.2% | 2025/06/30 | 2025/07/08 | | | | | | |
| Test | 0:20 | 0:00 | 7.5% | 2025/06/30 | 2025/07/08 | | | | | | |
| Postmortem | 0:25 | 0:00 | 9.7% | 2025/07/01 | 2025/07/08 | | | | | | |

# スケジュール

| 期間開始日 | 期間終了日 | 計画時間 | 累積計画時間 | 累積計画価値 | 実績時間 | 累積実績時間 | 獲得価値 |
|---|---|---|---|---|---|---|---|
| 2025/06/29 | 2025/06/29 | 2:00 | 2:00 | 44.4% | 0:00 | 0:00 | 0% |
| 2025/06/30 | 2025/06/30 | 2:00 | 4:00 | 90.3% | 0:00 | 0:00 | 0% |
| 2025/07/01 | 2025/07/01 | 3:00 | 7:00 | 100% | 0:00 | 0:00 | 0% |
| 2025/07/02 | 2025/07/02 | 2:00 | 9:00 | 100% | 0:00 | 0:00 | 0% |
| 2025/07/03 | 2025/07/03 | 1:00 | 10:00 | 100% | 0:00 | 0:00 | 0% |
| 2025/07/04 | 2025/07/04 | 0:00 | 10:00 | 100% | 0:00 | 0:00 | 0% |
| 2025/07/05 | 2025/07/05 | 0:00 | 10:00 | 100% | 1:20 | 1:20 | 0% |
